



Installation Utility Completion SIGN-OFF Sheet

Model: 945GENESIS

INSTALLATION SITE LOCATION

Location Name:
Address:
City:
State:
Zip Code:
Onsite Contact Name:
Onsite Contact Phone:

VENDOR INFORMATION


WebstaurantStore
40 Citation Lane
Lititz, PA 17543

General Inquiries & Accounts Payable:
installations@readykitchenwarranty.com
Hours of Operation: 8am – 4pm EST

Please check each box and sign this form as soon as the utility hookups are completed. Your equipment can only be shipped and installation scheduled after a completed and signed form has been received.

	- Receptacle type: NEMA L6-20R 3 Prong twist-lock - Breaker Panel: 20 Amp dedicated 220V single phase circuit - Nominal power rating: 2.9-3.8kW - Power Supply: 208-240V, 60Hz INSTALLED: Yes No		The receptacle, water shut-off valve and drain pipe must be within 3 feet (36") of the center of the location (footprint) of the machine. ↑ ↓ Ideal under counter space for softener: 30" (minimum requirement: 26"). ↑ ↓ INSTALLED: Yes No
	- Access hole with collar (no sharp edges) - Located centrally under machine for water and drain hose - Diameter: Minimum 3" INSTALLED: Yes No		INSTALLED: Yes No
	- Water shut-off valve with 3/8" compression fitting - Back flow preventer in accordance with local requirements INSTALLED: Yes No		Required machine and optional water filter clearances according to Utility Specifications sheet INSTALLED: Yes No
	- Drain pipe to floor drain - Copper or PVC in accordance with local health codes and regulations - Diameter: 1.5" or larger INSTALLED: Yes No		DAY OF INSTALLATION: - Minimum 2lbs each regular and decaf beans for machine calibration - Minimum 1 gal. and 5 each cup size for machine calibration ONSITE: Yes No

Curtis Genesis Utility Specifications

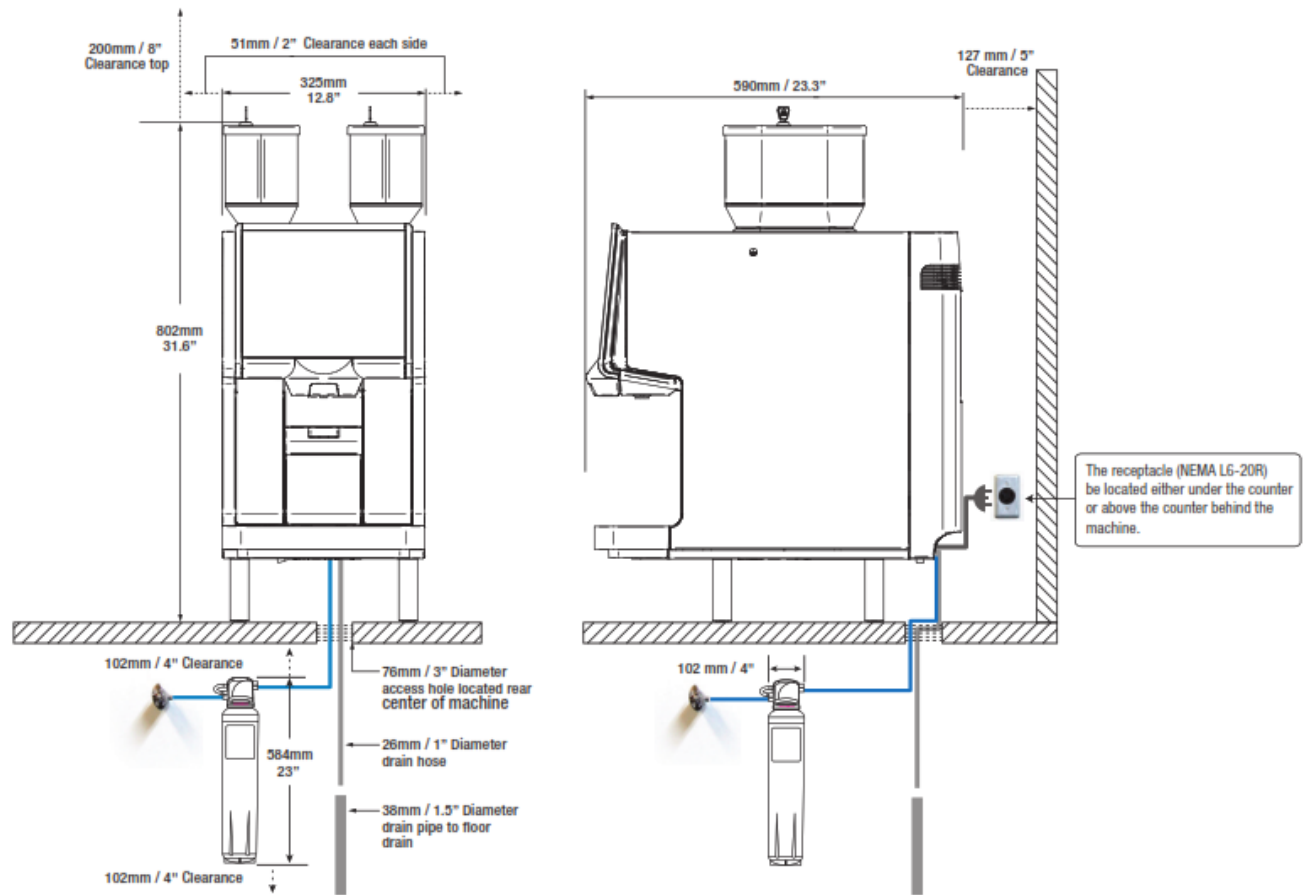

Notes: Access hole is only required if any of the utility hook-ups are located under the counter.

For technical assistance with installation please contact:
Wilbur Curtis Company
800-421-6150
www.wilburcurtis.com

Name of Person Declaring Utility Completion

Signature

Date

PENALTY NOTICE

All plumbing and electrical hook-ups must be completed and this form signed and returned before scheduling installation. If installation cannot be completed due to site conditions (i.e. no power, water, drain hook-up or product for calibration) a Penalty Charge of \$400.00 USD or the incurred install cost, whichever is great, will be assessed. This penalty will be spent for each subsequent visit upon which the site is not ready for installation. In the event there is any standby time spent by the technician onsite awaiting completion of site conditions, additional charges will apply.
